

WORKS EXECUTED UNDER MGNREGA

District Rural Development Agency Chamba Distt. Chamba (H.P)

Name of Block : Bhattiyat

Name of Panchayat : Chhallara

Name of Work : Providing Flood Protection Work to save the cultivation land of Gram Panchayat Chhallara along the Chanhal Khadd Right and Left Banks.

Estimated Cost : 10.00 Lacs

Yea : 2010-11

Executing Agency :I.P.H Sub Division Sihunta.







Name of Block : Bhattiyat

Name of Panchayat : Thulel

**Name of Work : Flow Irrigation Scheme Thulel (SH: Providing
crate work to save the Kuhl from land sliding
beyond RD 1180) .**

Estimated Cost : 5.00 Lacs

Year : 2010-11

Executing Agency :I.P.H Sub Division Sihunta





Name of Block : Bhattiyat

Name of Panchayat : Motla


Name of Work : Flow Irrigation Scheme lower Motla (SH: Construction of Head weir and wire crate embankment)

Estimated Cost : 5.00 Lacs

Year : 2010-11

Executing Agency :I.P.H Sub Division Sihunta.



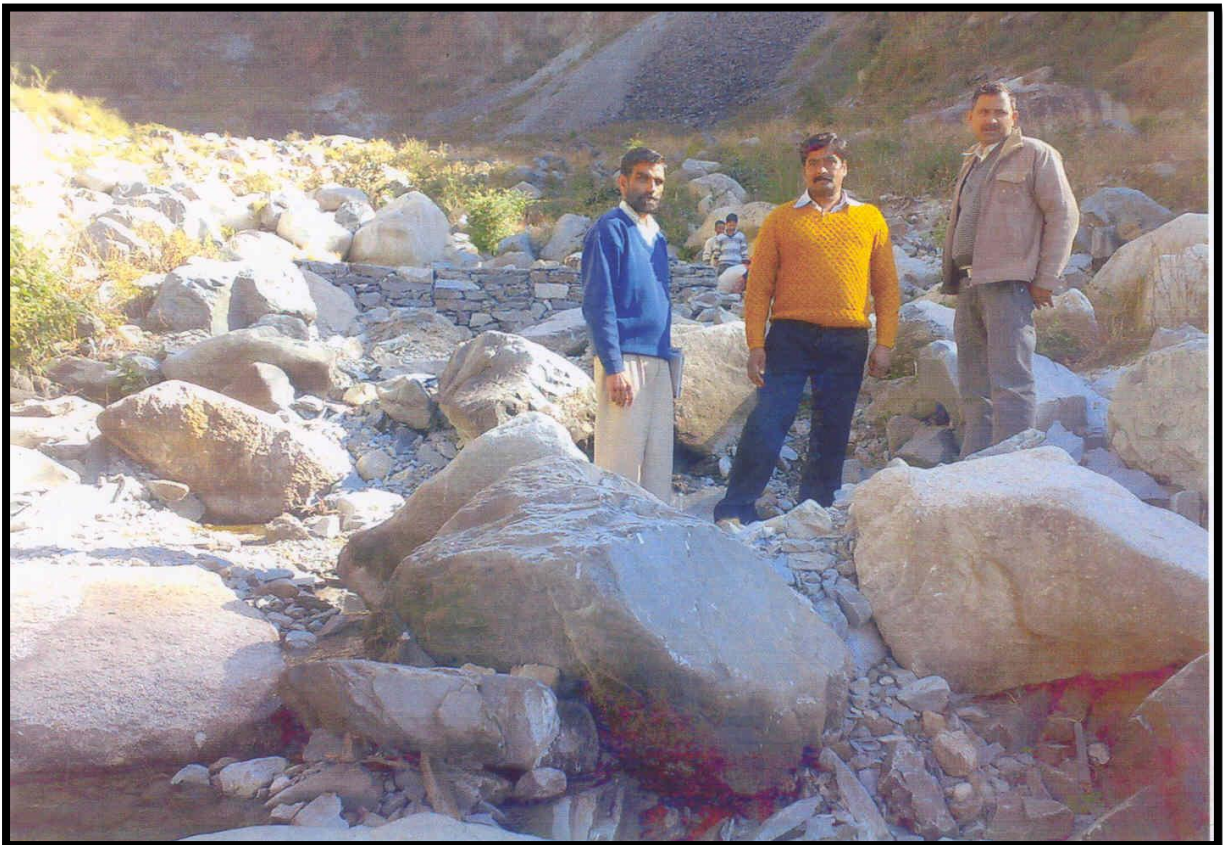

Name of Block : Bhattiyat

Name of Panchayat : Rajain

Name of Work : Flow Irrigation Scheme Rajain Saroga RD 8000 to 20800(SH:Removal of Slip and construction of damaged edge walls)

Estimated Cost : 10.00 Lacs

Year : 2010-11

Executing Agency :I.P.H Sub Division Sihunta.









Name of Block : Tissa

Name of Panchayat :

Name of Work : C/O Van Sarovar at Pugthala beat.

Estimated Cost : .60 Lacs

Year : 2010-11

Executing Agency :Forest Department, Churah Forest Division.





Name of Block : Chamba

Name of Panchayat : Pukhari

Name of Work : C/O Kuhal at Tatlahar.

Estimated Cost : 3.00 Lacs

Year : 2008-09

Executing Agency :Gram Panchayat

Mandays Generated : 1638

Family Benifited : 15-20

Area Irrigated : 2-3 Hact.

Brief History : The residents of village Tatlahar used to cultivate paddy until a decade ago with the help of kachha kuhal from Tatlahar. Due to maintenance & heavy seasonal flow, the kuhal was damaged and out of use for a decade. On the demand of villagers, the restoration of the kuhal was taken up under MGNREGA in 2008-09. The work was taken up in November 2008. A 300 mtr long (.30x.90x.25) open channel in Cement masonary was executed.

Now the idle flow of Tatlahar is being harnessed for cultivation of paddy and vegetable crops which has strengthened the livelihood security of local villager. This kuhal irrigates (2-3 Hect.) area and benefits to approximately 15-20 families.







Name of Block : Chamba

Name of Panchayat : Pukhari

Name of Work : C/O Kuhal at Bari Nala.

Estimated Cost : 1.50 Lacs

Year : 2008-09

Executing Agency :Gram Panchayat

Mandays Generated : 818

Family Benifited : 15-20

Area Irrigated : 1.5-2.5 Hact.

Brief History

: The residents of village Bari used to cultivate paddy until a decade ago with the help of kachha Kuhal from Ballu nalla. Due to maintenance & heavy seasonal flow, the kuhal was damaged and out of use for a decade. On the demand of villagers, the restoration of the Kuhal was taken up under MGNREGA in 2009-10. The work was taken up in 30.9.2009. A 150 mtr long(300x.90x.25) open channel in stone/ c.concrete was executed.

Now the idle flow of Ballu nalla is being harnessed for cultivation of paddy and vegetable crops which has strengthened the livelihood security of local villager. This kuhal irrigate (1.5-2.05 hect) area benefits to approximately 15-20 families.





Name of Block : Chamba

Name of Panchayat : Kohladi

Name of Work : C/O Channel Kuhal Kakaila Nala 1500 mtrs..

Estimated Cost : 9.60 Lacs

Year :

Executing Agency :Gram Panchayat

Mandays Generated : 2955

Family Benifited : 25

Area Irrigated :

Brief History : The Kuhal has been conduction for approximately 25 families covering both sides of cultivated land for ST & BPL families in village Daresh, Kaloti & Kohladi. This Kuhal is constructed in 3 steps. Total length which has been completed till date is 720 mtrs.





Name of Block : Chamba

Name of Panchayat : Kohladi

Name of Work : C/O Channel Kuhal Chaili Nala 600 mtrs..

Estimated Cost : 3.84 Lacs

Year :

Executing Agency :Gram Panchayat

Mandays Generated : 1619

Family Benifited : 20

Area Irrigated :

Brief History : The Kuhal has been conduction for approximately 20 families covering both sides of cultivated land for ST & BPL families in village Chaili & Trag . This Kuhal is constructed in 3 steps. Total length which has been completed till date is 350 mtrs.



Name of Block : Chamba

Name of Panchayat : Dulahar

Name of Work : C/O Water Storage Tank at Lotuien.

Estimated Cost : 1.00 Lacs

Year : 2009-10

Executing Agency :Gram Panchayat

Mandays Generated : 550

Family Benifited : 11-12

Area Irrigated : 0.5 Hect.

Brief History : The residents of villages in GP Dulahar were hampered in taking up agriculture as a livelihood activity due to lack of irrigation. The above project was taken up under MGNREGA in the year 2009-10. The tap of flow of Lotuien nalla which was going waste? The above work was taken up in the month of October 2009. A 2.7x2.40x2.10 of 13.61 cum capacity tank R/R Stone masonry is constructed which is fed by the Lotuien nalla with the help of 1.5 inch PVC pipe. With the help of the water so harnessed (0.5 Hect) area is being cultivated. The local farmers are growing vegetable like peas, cabbage etc. An apple orchard with 200 trees id being also raised with the help of irrigation from this tank.



Name of Block : Chamba

Name of Panchayat : Prahavi

Name of Work : C/O Water Storage Tank at Dhaka.

Estimated Cost : 1.00 Lacs

Year : 2008-09

Executing Agency :Gram Panchayat

Mandays Generated : 545

Family Benifited : 11-12

Area Irrigated : 0.4 Hect.

Brief History : The residents of villages Dhaka in GP Prahavi were hampered in taking up agriculture as livelihood activity due to lack of irrigation. The above project was taken up under MGNREGA in the year 2009-10. The tap of flow of Lotuian nalla which was going waste? The above work was taken up in the month of August 2008. A 2.70Mx2.40Mx1.8 of 11.66 cum capacity tank R/R Stone masonry is constructed which is fed by the nearby sources with the help of 1.5 inch PVC pipe. With the help of the water so harnessed (0.4 Hect) area is being cultivated. The local farmers are growing vegetable like onion, tomato with the help of irrigation from this tank.





Name of Block : Chamba

Name of Panchayat : Cheel Bangla

Name of Work : C/O Water Drainage at Khotu to Bairi Nali.

Estimated Cost : .60 Lacs

Year : 2009-10

Executing Agency :Gram Panchayat

Family Benifited : 12



Name of Block : Chamba

Name of Panchayat : Dulahar

Name of Work : C/O Pucca Path village Shadalu.

Estimated Cost : 1.00 Lacs

Year : 2009-10

Executing Agency :Gram Panchayat

Mandays : 465

Family Benifited : 15



Name of Block : Mehla

Name of Panchayat : Mangla

Name of Work : C/O Water Harvesting Dam at Bhatalwan Nalla.

Estimated Cost : 5.751 Lacs

Year : 2009-10

Executing Agency :Gram Panchayat

Mandays Generated : 3137

Family Benifited : 25



Name of Block : Bhattiyat

Name of Panchayat : Bathri

Name of Work : C/O Water Harvesting Check Dam 20 mtrs at Dadra Nala

Estimated Cost : 6.39 Lacs

Year :

Executing Agency :Gram Panchayat

Family Benifited : 25

Area Irrigated : 6-7 Hact

Brief History : Initially in this work we peoposed one check dam 20 mtrs and one irrigation tank of capacity about 150000 ltr. But now as per rerequirement of villagers of village Dadra be revised the estimate and constructed irrigation tank of capacity 250000 ltr. In the scheme about 25 families ST, SC & geneal families of Dadra village take the benefit and cultivated six to seven Hact of land and proposed check dam for useful of prevention of soil erosion and recharge of water table.



Name of Block : Tissa

Name of Panchayat : Kareri

Name of Work : C/O Protection work Sapdi Behi.

Estimated Cost : 1.50 Lacs

Year : 2010-11

Executing Agency :Gram Panchayat



Name of Block : Tissa

Name of Panchayat : Saprot

Name of Work : C/O Irrigation Kuhal Village Baroga to Asund..

Estimated Cost : 4.00 Lacs

Executing Agency :Gram Panchayat

Family Benifited : 10

Area Irrigated : 1 Hact

Mandays : 100

Year : 2010-11

Executing Agency :Gram Panchayat



Name of Block : Tissa

Name of Panchayat : Sanwal

Name of Work : C/O Panihara at Ansar.

Estimated Cost : 1.50 Lacs

Executing Agency :Gram Panchayat

Family Benifited : 25

Year : 2010-11

Executing Agency :Gram Panchayat



Name of Block : Tissa

Name of Panchayat : Thanneikothi

Name of Work : C/O Panihara at Sukiyani.


Estimated Cost : 1.50 Lacs

Executing Agency :Gram Panchayat

Family Benifited : 20

Year : 2010-11

Executing Agency :Gram Panchayat

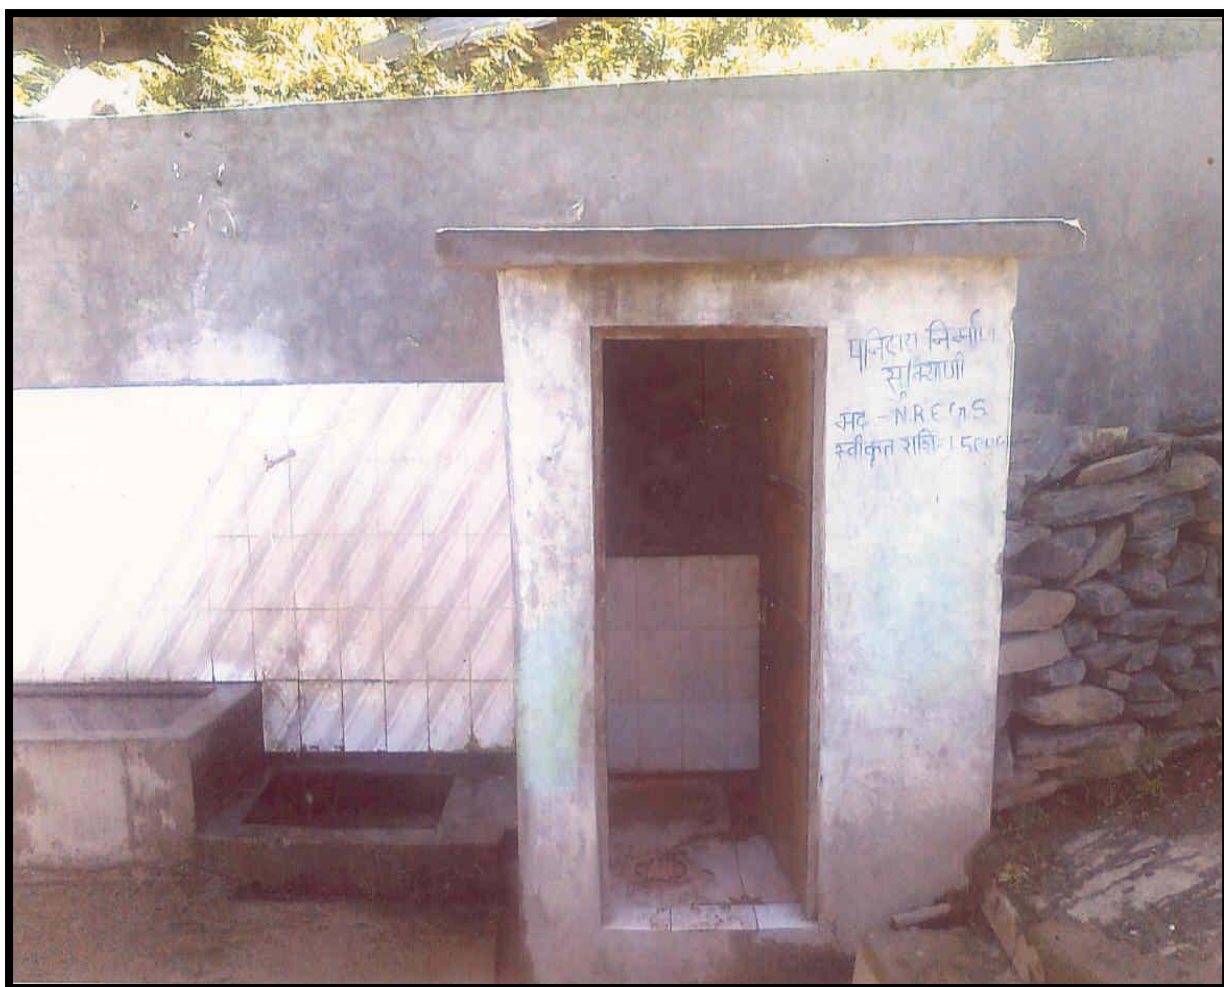

Name of Block : Salooni

Name of Panchayat : Wangal

Name of Work : C/O Van Sarover Ghatta Gala.


Estimated Cost : 1.76700 Lacs

Executing Agency :Gram Panchayat

Year : 2010-11

Mandays : 1083

Executing Agency :Gram Panchayat

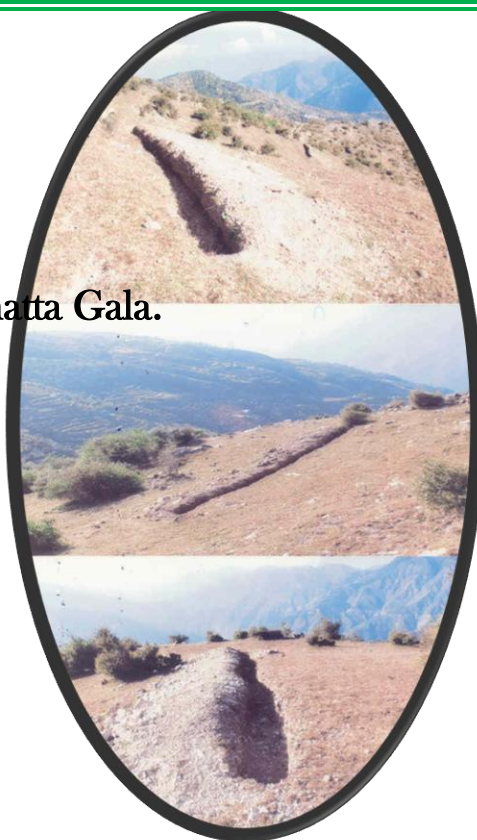

Name of Block : Salooni

Name of Panchayat : Simni

Name of Work : C/O Van Sarover Drabla Nalla.

Estimated Cost : 1.95900 Lacs

Executing Agency :Gram Panchayat

Year : 2010-11

Mandays : 845

Executing Agency :Gram Panchayat



